

Project Overview

In August both Phase 2 areas were vacated and turned over to Bouten for construction barriers and demolition efforts. The birthing microphase A1 South pathway was completed and open for occupancy, after which the A1 North area was captured within the construction barriers.

The generator transfer switch change overs were completed in conjunction with the AHU-1 Fan Wall improvements.

Phase 2 Paradise and Butch interior demolition efforts are substantially complete, with overhead and under ground rough in progressing to allow wall framing to begin.

Phase 2 Butch structural additions are underway with the primary structure completed.

Submittal & RFI Log

Submittals being tracked: 486
Submittals in for review: 3
RFIs in for review: 7
RFIs processed: 137

Schedule Update

Data date: 08/31/2026
Percent complete per overall schedule: 37%
Percent complete per overall task: 54%
Schedule variance in days: 0 working days – Substantial Completion December 21, 2027


Summary Report for Progress Schedule:

Paradise – Future Same Day Services & OR 5 – Overall demolition completed with slab layout and concrete cutting completed. West side underground rough in and slab trench pour back completed. Pneumatic Tubing Phase 1 phlebotomy blood draw completed with validation tested completed. Wall framing underway.

Butch – Future Vestibule & ED Entry – Exterior steel structure erected. Interior demolition completed with temporary interior wall structure in place to allow exterior wall demolition activities.

Infrastructure – Generators and Automatic Transfer Switches – Final (2) ATS change overs completed with vault layout for ATS OS and concrete base design being coordinated.

Area Map

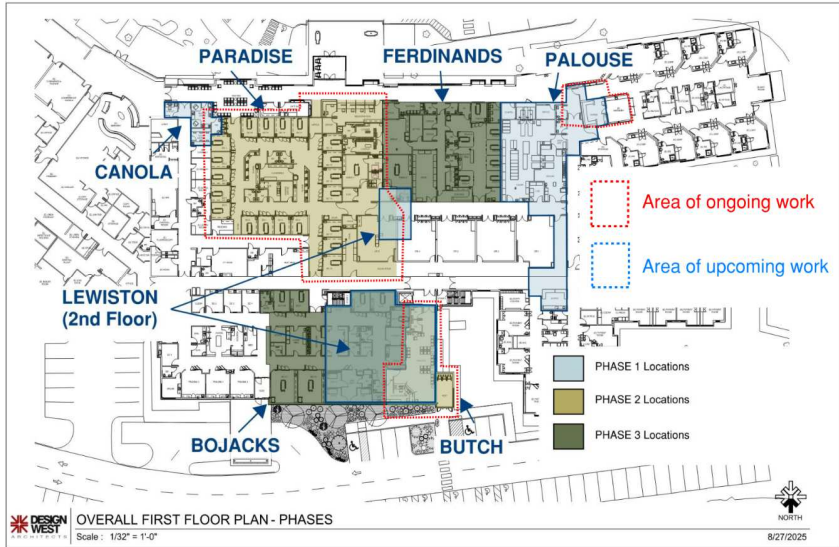


Project Spotlights

Turn over for occupancy – Birthing Phase A1 South.
Paradise underslab saw cutting complete for rough in.
Structural Steel started at Butch vestibule.

Progress Photos



Butch Steel - Underway

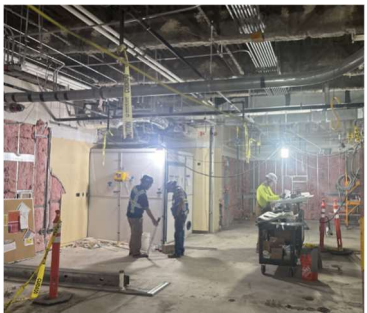


Paradise - Layout



Paradise – Slab Prep



Paradise – Slab Rough-in

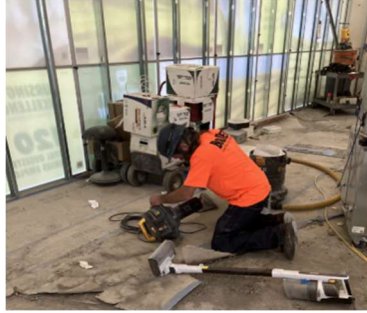

Paradise – N Reception



Butch Steel – Top Out



Exterior – Butch Demo



Paradise – Slab Pour Backs



Paradise – Box Walk

Upcoming Activities

- Wall framing and rough in to progress within Paradise.
- Interior steel structure support members being field measured and fabricated to align with overhead utility rough in assemblies.
- Butch vestibule exterior wall demolition and fireproofing.

Permits & Inspection Status

- Compaction and Concrete for exterior improvements.
- Fire Alarm coordination with voice & tone zones.
- Plumbing rough in underslab for pour backs.
