

Project Overview

In September progress continued in Phase A1 for the birthing station, Phase 2 Butch, Paradise and the North Registration areas.

All locations have completed under slab rough in and slab pour backs. Both overhead rough in and framing is substantially complete within the Paradise west area.

Steel detailing is ongoing for the overhead support areas within Paradise east for the boom arms in the Operating Room and future Endoscopy Room.

Turn over of the A1 birthing area is on schedule to turn over towards the end of October with the north registration area following in November.

Submittal & RFI Log

Submittals being tracked: 490
Submittals in for review: 2
RFIs in for review: 3
RFIs processed: 159

Schedule Update

Data date: 09/30/2026
Percent complete per overall schedule: 41%
Percent complete per overall task: 59%
Schedule variance in days: 0 working days – Substantial Completion December 21, 2027

Summary Report for Progress Schedule:


A1 – Birthing Nurses Station. Wall cover completed and first coat of paint ahead of casework installation.

Paradise – Future Same Day Services & OR 5 – West side framing completed and in wall rough in ongoing. East side underground rough in and slab trench pour back completed. North registration wall framing completed and in wall rough in ongoing.

Butch – Future Vestibule & ED Entry – Steel for structural rigidity completed to allow temporary interior wall structure and sequence for exterior wall demolition activities to commence. Slab on grade pour for vestibule entry and steel fire proofing pending.

Infrastructure – Exterior ATS vault layout and design completed, curb for pre-cast vault being formed for October completion.

Area Map

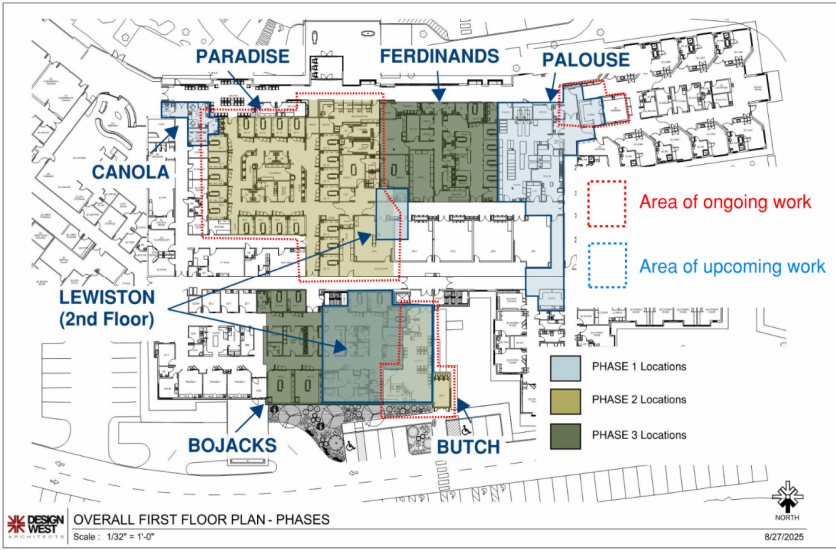


Project Spotlights

All underground utilities completed and slab pour backs in place.
Paradise OR sprinkler main relocation for ceiling heights.
Interior steel assembly in place for north registration area.

Progress Photos




Butch Slab on Grade Pour

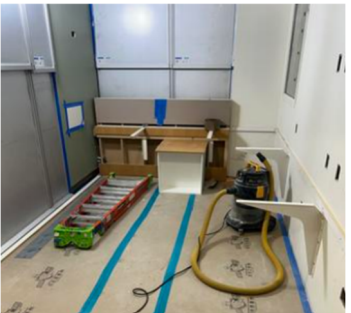

A1 Nurses Station



Vault Curb Prep

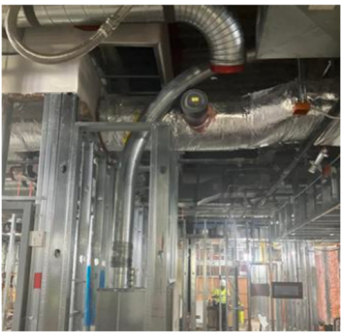

Paradise – OH Rough-in




Butch – Temp Wall Insulation




Paradise Fire Penetrations



Butch Slab on Grade Prep

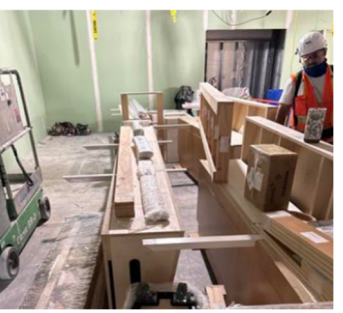

Casework for N. Registration

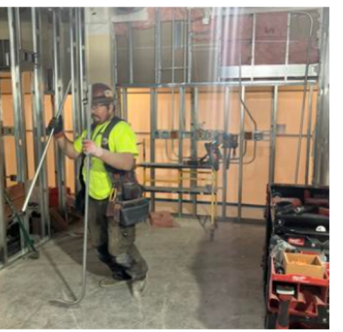

Paradise – Wall Rough In

Upcoming Activities

- Paradise overhead utility shutdown for ceiling elevations.
- Wall framing and rough in to progress within Paradise.
- Interior steel structure support members fabrication to align with overhead utility rough in assemblies.
- Butch vestibule exterior wall demolition and fireproofing.

Permits & Inspection Status

- Compaction and Concrete for exterior improvements.
- Fire Alarm coordination with voice & tone zones.
- Plumbing overhead and wall rough in.
- Temp Fire Protection for Life Safety.
