



PULLMAN
REGIONAL
HOSPITAL

PATIENT CARE EXPANSION UPDATE

Less Wait, Less Travel, More Access to Exceptional Healthcare




August 7, 2026 Update

PROGRESS UPDATE:

33% COMPLETE!

PHASE 1:

- ☑ New 2nd floor laboratory
- ☑ Main floor blood draw station
- ☑ New central sterile

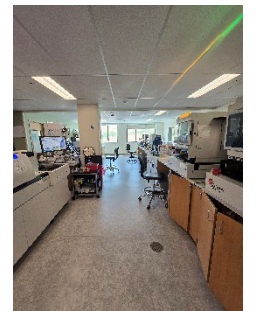

NEW TECHNOLOGY:

- ☑ Central sterile technology
- ☑ CT machine
- ☑ Nuclear medicine machine
- ☑ BirthPlace baby warmers



COMPLETE & IN PROGRESS:





ATS-W (Automatic Transfer Switch W) Complete!

AHU: August 6-9 (Air Handler Unit Replacement)



- No circulating air in ORs 2-4. OR 1 receives temporary air supply during this time.
- Central sterile and related areas without circulating air for four days; instrument reprocessing not possible. **Clinics advised to avoid scheduling procedures August 6-7 to prevent running out of instruments.** Central Sterile will not be able to reprocess instruments from Aug 5th at 1600 until Aug 10th.
- Only **emergency** surgeries allowed during shutdowns per code requirements.

Phase 2: Paradise (June 26 – Spring 2027)

- New centralized registration, centralized Same-Day, Endoscopy Suites & 5th OR

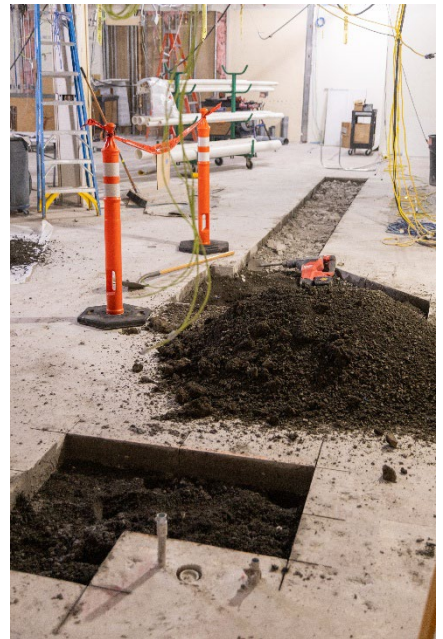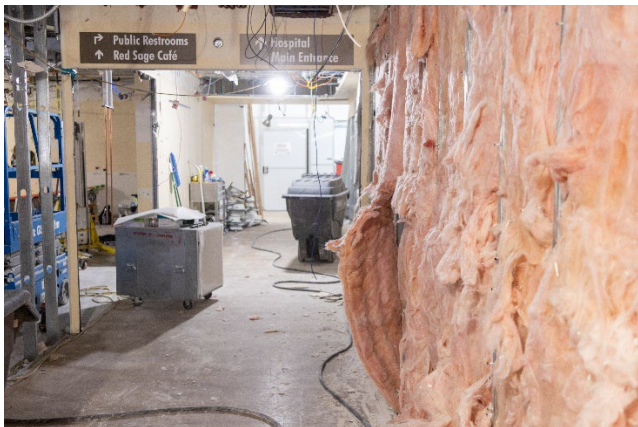


CONSTRUCTION PHASES BEFORE & AFTER:

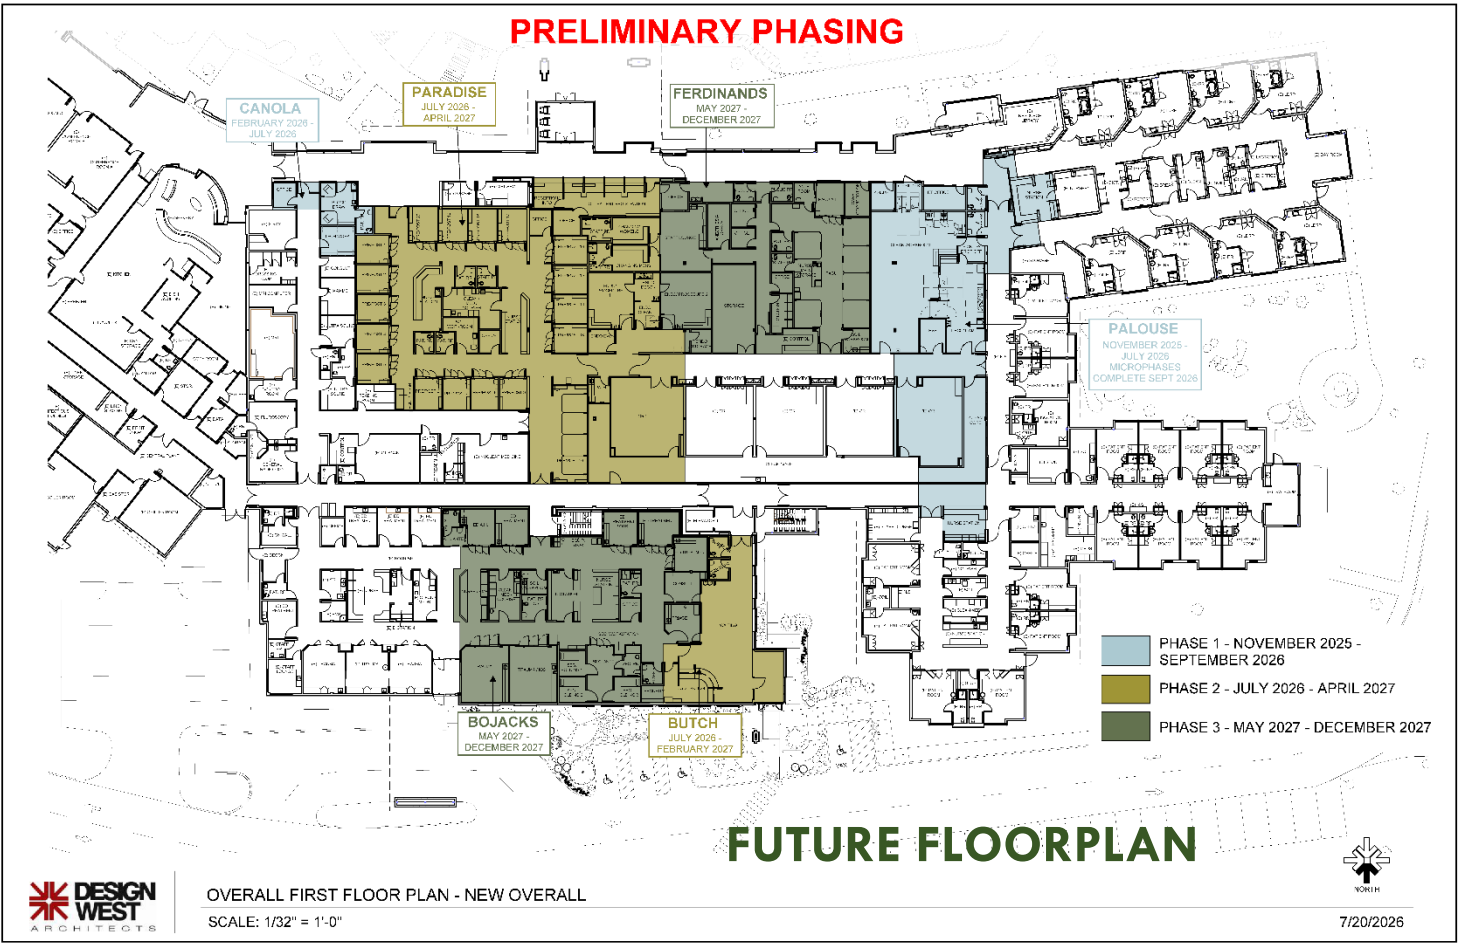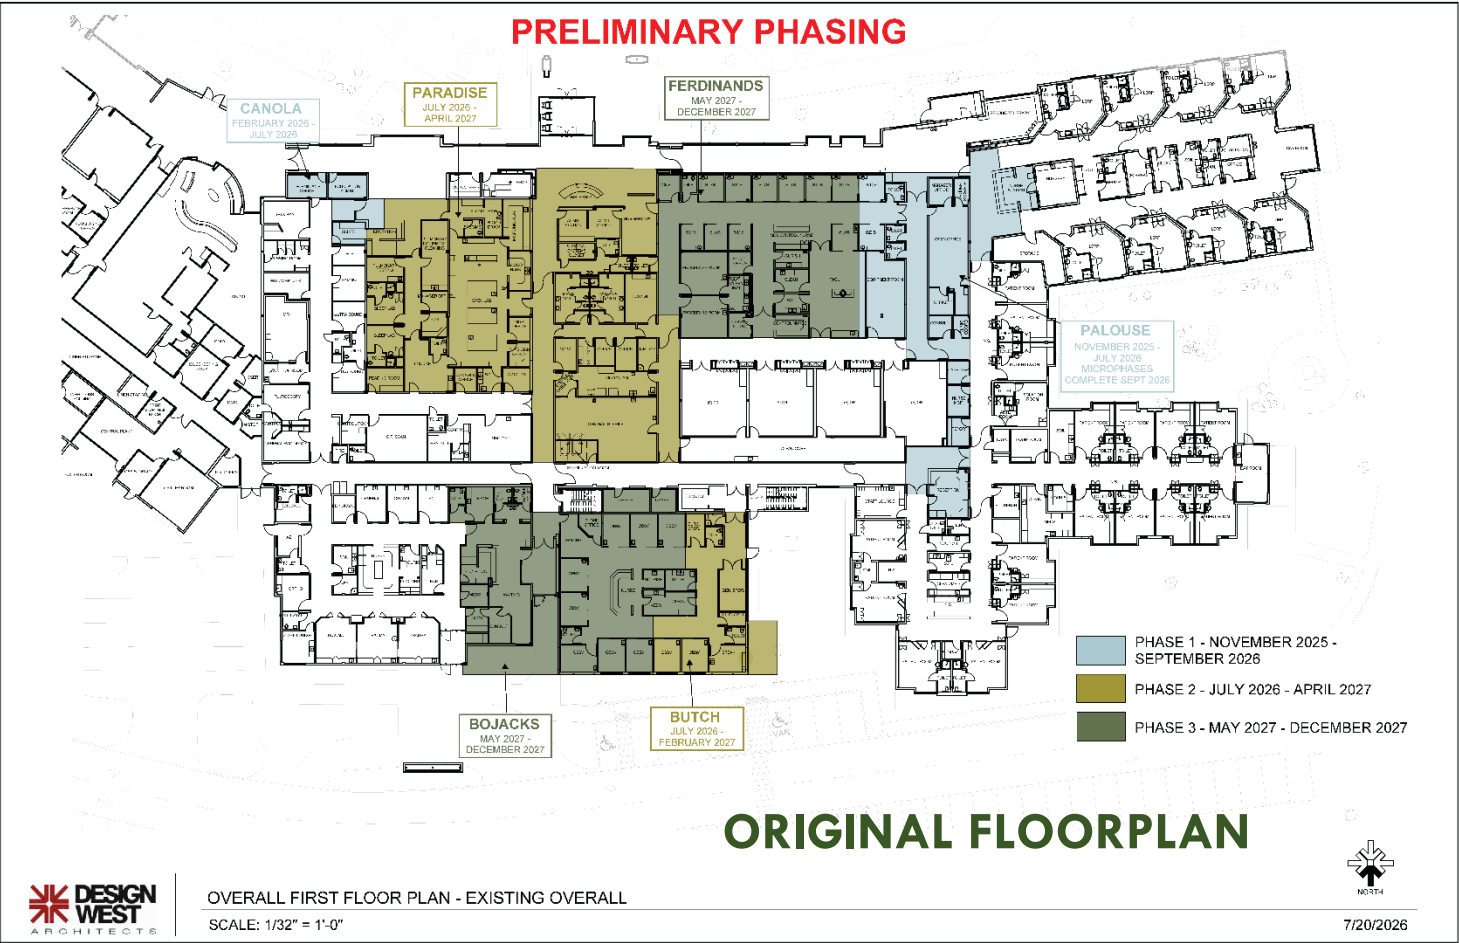

IN PROGRESS:


Phase 2: Butch (July 2026 – February 2027): New ED entrance, restrooms, waiting area and registration

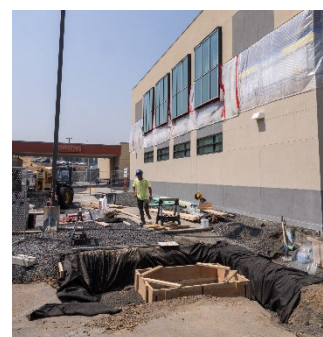

WAYFINDING UPDATES:

Starting the week, of August 10: Staff prox entrance from rear of building (between Same Day South and ICU) will not be accessible during Butch Phase of construction.

August 10: BirthPlace Access through MSU only for staff, patients and visitors. Work will start on the main entrance to BirthPlace starting August 10 through the end of September. See routes in blue.

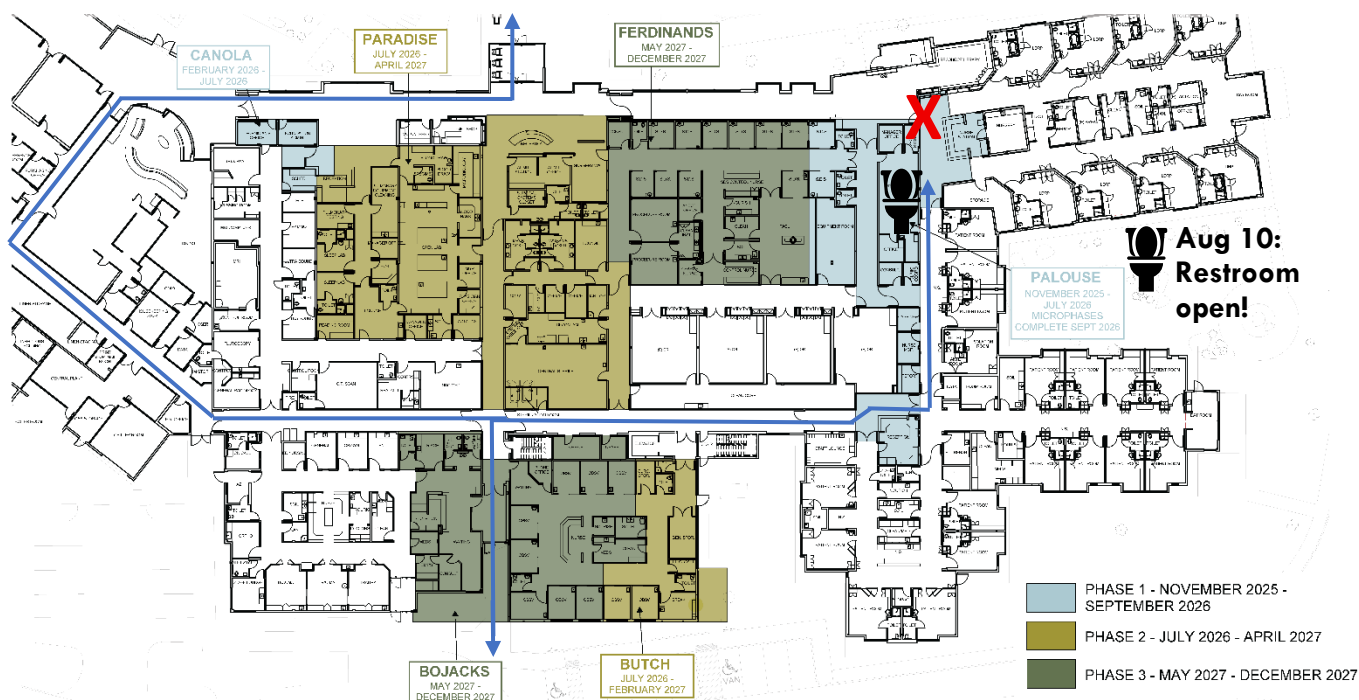

Stay in the know:
pullmanregional.org/internal
